


Appendix A Master Programme

Activity ID	Activity Name	Primary Constraint	At Completion Duration	Current Start	Current Finish	Actual Start	Actual Finish	Late Start	Late Finish	Total Float	Activity % Complete	M28 Remarks	2017												2018												2019												2020												2021												2022												2023												2024												2025																																			
													1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12																								
EP_SP_66_12-WP-3-M28 Programme for Design and Construction Works WP3-M28																																																																																																																																																
EP_SP_66_12-WP-3-M28.01 Key Dates																																																																																																																																																
EP_SP_66_12-WP-3-M28.01.1 Contractual Key Dates																																																																																																																																																
EP_SP_66_12-WP-3-M28.01.1.1 Design and Construction Phase																																																																																																																																																
01-1000	Contract Award/Date of Acceptance of Tender	Mandatory Start	0			22-Nov-17 A					100%	Contract Award/Date of Acceptance of Tender, 22-Nov-17 A																																																																																																																																				
01-1010	Date of Commencement of the Design and the Works	Mandatory Start	0			15-Dec-17 A					100%	Date of Commencement of the Design and the Works, 15-Dec-17 A																																																																																																																																				
01-1015(3)(M12)	Original Substantial Completion of the Works	Mandatory Finish	0		27-Jul-24		27-Jul-24*		27-Jul-24	0	0%																																																																																																																																					
01-1015-1(3)(M12)	Extension of time granted (Claim No.1 to No.8 & No.10 to No.11)		41	27-Jul-24	13-Sep-24	27-Jul-24	13-Sep-24	27-Jul-24	13-Sep-24	0	0%																																																																																																																																					
01-1016(3)(M18)	Extension of time granted without holidays (Claim No.12 to No.26)	Mandatory Finish	138	13-Sep-24	29-Jan-25	13-Sep-24	29-Jan-25*		29-Jan-25	0	0%																																																																																																																																					
01-1020	Extended Substantial Completion of The Works	Mandatory Finish	0		29-Jan-25		29-Jan-25*		29-Jan-25	0	0%	29-Jan-2025 (noon)																																																																																																																																				
EP_SP_66_12-WP-3-M28.01.2 Operation Phase																																																																																																																																																
01-1030	Commencement of Operation	Mandatory Start	0	30-Jan-25		30-Jan-25*		30-Jan-25		0	0%																																																																																																																																					
01-1230	Issue Certificate of Completion of the Works (56 days after Substantial Completion)	Mandatory Finish	0	26-Mar-25		26-Mar-25*		26-Mar-25		0	0%																																																																																																																																					
EP_SP_66_12-WP-3-M28.01.2 Planned Completion Dates																																																																																																																																																
01-1040	Incoming Power Energization to IWMF Substation		0	10-Sep-24		10-Sep-24		02-Jun-24		-101	0%																																																																																																																																					
01-1050	Export Power to Grid		0	24-Sep-24		24-Sep-24		06-Sep-24		-19	0%																																																																																																																																					
01-1060	Issuance of FS Certificate		0	08-Jan-25		08-Jan-25		23-Aug-24		-139	0%																																																																																																																																					
01-1070	Completion of Civil Provision for Transmission		0	04-Jan-23		04-Jan-23		02-Jan-23		-3	0%																																																																																																																																					
01-1080	Commencement of C1.3.4.11 System Commissioning Test		0	06-Oct-24		06-Oct-24		15-Jun-24		-113	0%																																																																																																																																					
01-1090	Completion of C1.3.4.11 System Commission Test		0	17-Jan-25		17-Jan-25		23-Aug-24		-148	0%																																																																																																																																					
01-1100	Completion of 90 Days Plant Commissioning Test		0	01-May-25		01-May-25		05-Dec-24		-148	0%																																																																																																																																					
01-1110(3)(M15)	Issue of Certificate of Substantial Completion for the Works	Finish On or Before	0	25-Jun-25		25-Jun-25*		29-Jan-25		-148	0%																																																																																																																																					
EP_SP_66_12-WP-3-M28.01.2 Dates of Site Possessions																																																																																																																																																
01-1120	Possession of Portion 1		0			15-Dec-17 A				100%		Possession of Portion 1.																																																																																																																																				
01-1130	Possession of Portion 1A		0			15-Dec-17 A				100%		Possession of Portion 1A.																																																																																																																																				
01-1140	Possession of Portion 1B		0			15-Dec-17 A				100%		Possession of Portion 1B.																																																																																																																																				
01-1150	Possession of Portion 2		0			30-Jan-25*		30-Jan-25		0	0%																																																																																																																																					
01-1160	Possession of Portion 3	Mandatory Finish	0	13-Dec-20		12-Jan-22		12-Jan-22		394	0%																																																																																																																																					
01-1170	Possession of Portion 4		0	13-Dec-20		13-Dec-20		12-Jan-22		394	0%																																																																																																																																					
01-1180	Possession of Portion 5		0	13-Dec-20		12-Jan-22		12-Jan-22		394	0%																																																																																																																																					
01-1190	Possession of Portion 6		0	17-Jul-24		17-Jul-24		27-Mar-24		-113	0%																																																																																																																																					
01-1200	Possession of Portion 7	Finish On or Before	0			05-Jan-18 A				100%		Possession of Portion 7.																																																																																																																																				
01-1210	Possession of Portion 7A	Finish On or Before	0			07-Dec-18 A				100%		Possession of Portion 7A.																																																																																																																																				
EP_SP_66_12-WP-3-M28.02 Contract Preliminaries																																																																																																																																																
EP_SP_66_12-WP-3-M28.02.0 General																																																																																																																																																
01-1220	Provision of Contractor All Risk Insurance (COC 24.1)	Finish On or Before	0			11-Dec-17 A				100%		Provision of Contractor All Risk Insurance (COC 24.1)																																																																																																																																				
01-1240	Provision of Employee Compensation Insurance (COC 25)	Finish On or Before	0			12-Dec-17 A				100%		Provision of Employee Compensation Insurance (COC 25)																																																																																																																																				
01-1250	Provision of Contractor's Professional Indemnity Insurance (COC 24.2(a))	Finish On or Before	0			11-Dec-17 A				100%		Provision of Contractor's Professional Indemnity Insurance (COC 24.2(a))																																																																																																																																				
EP_SP_66_12-WP-3-M28.02.1 Employer's Accommodations																																																																																																																																																
02-1000	Establishment of Employer's Off Island Temporary Accommodation	Finish On or Before	87	02-Apr-22	27-May-22	03-Jan-18 A	27-May-22	27-Dec-21	21-Feb-22	-96	100%	Establishment of Employer's Off Island Temporary Accommodation, 31-Mar-18 A																																																																																																																																				
02-1020	Establishment of Employer's On Island Temporary Accommodation		56	02-Apr-22	27-May-22	02-Apr-22	27-May-22	27-Dec-21	21-Feb-22	-96	0%																																																																																																																																					
EP_SP_66_12-WP-3-M28.02.2 Establishment of Environmental Monitoring Stations																																																																																																																																																
02-1030	Establishment of Air Quality Monitoring Station at Portion 3 (12m Prior to T&C)		180	07-Oct-21	04-Apr-22	07-Oct-21	04-Apr-22	12-Jan-22	11-Jul-22	97	0%																																																																																																																																					
02-1040	Establishment of Air Quality Monitoring Station at Portion 4 (12m Prior to T&C)		180	07-Oct-21	04-Apr-22	07-Oct-21	04-Apr-22	12-Jan-22	11-Jul-22	97	0%																																																																																																																																					
02-1050	Establishment of Air Quality Monitoring Station at Portion 5 (12m Prior to T&C)		180	07-Oct-21	04-Apr-22	07-Oct-21	04-Apr-22	12-Jan-22	11-Jul-22	97	0%																																																																																																																																					
EP_SP_66_12-WP-3-M28.02.3 Erection of Concrete Batching Plant on Artificial Island																																																																																																																																																
02-1080	Erection of Concrete Batching Plant		60	28-May-22	26-Jul-22	28-May-22	26-Jul-22	03-Jan-22	04-Mar-22	-145	0%																																																																																																																																					
02-1090	Commissioning of Concrete Batching Plant		30	27-Jul-22	25-Aug-22	27-Jul-22	25-Aug-22	04-Mar-22	03-Apr-22	-145	0%																																																																																																																																					
02-1100	Operation of Concrete Batching Plant		500	26-Aug-22	07-Jan-24	26-Aug-22	07-Jan-24	22-Jun-22	04-Nov-23	-65	0%																																																																																																																																					
02-1110	Demobilization of Concrete Batching Plant		60	08-Jan-24	07-Mar-24	08-Jan-24	07-Mar-24	04-Nov-23	03-Jan-24	-65	0%																																																																																																																																					
EP_SP_66_12-WP-3-M28.02.4 Establishment of Public Relation Office																																																																																																																																																
02-1060	SO issue instruction for provision of IWMF Information Office(s) (IWMFIO) (Tentative)		0			31-Mar-20		31-Mar-20		384	0%																																																																																																																																					
02-1070(2)	Submission and approval for location, layout and details of IWMF Information Office(s)		0	21-Apr-20	19-Jun-20	21-Apr-20	19-Jun-20	10-May-21	09-Jul-21	384	0%																																																																																																																																					
02-1120(2)	Establishment of IWMF Information Office(s)		90	20-Jun-20	17-Sep-20	20-Jun-20	17-Sep-20	09-Jul-21	07-Oct-21	384	0%																																																																																																																																					
02-1140(2)	Decommissioning of IWMF Information Office(s)		30	29-Jan-26	28-Feb-26	29-Jan-26	28-Feb-26	29-Jan-26	28-Feb-26	0	0%																																																																																																																																					
EP_SP_66_12-WP-3-M28.02.5 Replacement of Onshore Crane at Portion 2																																																																																																																																																
02-1150(2)	Replace Crane No. 1 (Incl. T&C)		90	30-Apr-25	28-Jul-25	30-Apr-25	28-Jul-25	02-Aug-25	31-Oct-25	94	0%																																																																																																																																					
02-1160(2)	Replace Crane No. 2 (Incl. T&C)		90	28-Aug-25	25-Nov-25	28-Aug-25	25-Nov-25	30-Nov																																																																																																																																								

Activity ID	Activity Name	Primary Constraint	At Completion Duration	Current Start	Current Finish	Actual Start	Actual Finish	Latest Start	Latest Finish	Total Float	Activity % Complete	M28 Remarks
05-1020	Ash Cranes	Start On or After	244			07-Sep-18 A	09-May-19 A				100%	
05-1030	Leachate Collection and Treatment	Start On or After	245			25-May-18 A	25-Jan-19 A				100%	
05-1040	Waste Water Treatment System	Start On or After	361			06-Jul-18 A	02-Jul-19 A				100%	
05-1050	Overall Plan Water Scheme	Start On or After	350			24-May-18 A	09-May-19 A				100%	
05-1060	Boiler Feed Water System	Start On or After	223			21-Mar-18 A	30-Oct-18 A				100%	
EP_SP_66_12-WP-3-M28.05.01.01.2	MSW treatment process design for mechanical treatment (2.1.02)		707	31-Mar-20	13-Jul-20	07-Aug-18 A	13-Jul-20	02-May-20	15-Aug-20	32		
05-1090	Mechanical Treatment Plant (2.1.02.01)	Start On or After	105	31-Mar-20	13-Jul-20	31-Mar-20*	13-Jul-20	02-May-20	15-Aug-20	32	0%	
05-1100	Desalination Plant and Boiler Water Treatment (Demin Unit) Plant (2.1.02.02)	Start On or After	345			07-Aug-18 A	18-Jul-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.01.3	Waste heat recovery and Power generation system (2.1.03)		323			24-May-18 A	12-Apr-19 A					
05-1110	Power Island (Steam Turbine Generator, Pressure Reducing and Desuperheating Station, Air Cooled Cond)	Start On or After	323			24-May-18 A	12-Apr-19 A				100%	
05-1120	Closed Circuit Cooling Water System	Start On or After	323			24-May-18 A	12-Apr-19 A				100%	
05-1130	Compressed Air Plants	Start On or After	232			04-Jul-18 A	21-Feb-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.01.4	Flue gas treatment process design for incineration (2.1.04)		270			15-Mar-18 A	10-Dec-18 A					
05-1070	Flue Gas Treatment System	Start On or After	242			15-Mar-18 A	12-Nov-18 A				100%	
05-1080	Boiler ash and APC residue handling and solidification	Start On or After	199			25-May-18 A	10-Dec-18 A				100%	
EP_SP_66_12-WP-3-M28.05.01.01.5	Logistic arrangement design for MSW and Ash and Residues (2.1.05)		384			05-Jul-18 A	24-Jul-19 A					
05-1140	Weighbridge Systems	Start On or After	152			05-Sep-18 A	04-Feb-19 A				100%	
05-1150	Waste Crane and Grapple System	Start On or After	221			05-Jul-18 A	11-Feb-19 A				100%	
05-1160	Mechanical Shredder	Start On or After	243			23-Nov-18 A	24-Jul-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.01.6	Site Master Layout Plan and Plant Layout (2.1.06)		766	31-Mar-20	31-May-20	27-Apr-18 A	31-May-20	31-Dec-20	03-Mar-21	275		
05-3020	Site Master Layout Plan and Plant Layout		766	31-Mar-20	31-May-20	27-Apr-18 A	31-May-20	31-Dec-20	03-Mar-21	275	65%	
EP_SP_66_12-WP-3-M28.05.01.01.7	Statutory Fire Compliance (2.1.25)		123	31-Mar-20	31-Jul-20	31-Mar-20*	31-Jul-20	10-Apr-19	26-Feb-21	209		
05-2990	Fire Safety Compliance	Start On or After	123	31-Mar-20	31-Jul-20	31-Mar-20*	31-Jul-20	10-Apr-19	10-Aug-19	-356	0%	
05-3000	Fire Engineering Report	Start On or After	123	31-Mar-20	31-Jul-20	31-Mar-20*	31-Jul-20	10-Apr-19	10-Aug-19	-356	0%	
05-3010	Fire Compartmentation / FS compliance	Start On or After	123	31-Mar-20	31-Jul-20	31-Mar-20*	31-Jul-20	26-Oct-20	26-Feb-21	209	0%	
EP_SP_66_12-WP-3-M28.05.01.02	AIP Ground Treatment, Reclamation, Seawall, Breakwater, Berth (2.2)		913	31-Mar-20	12-Aug-20	12-Feb-18 A	12-Aug-20	26-Nov-19	20-Jul-21	341		
05-1170	Deep Cement Mixing Design (2.2.00)	Start On or After	136			27-Mar-18 A	10-Aug-18 A				100%	
05-1180	Ground Investigation Proposal (2.2.01.01)	Start On or After	143			12-Feb-18 A	05-Jul-18 A				100%	
05-1190	Preliminary Geotechnical Interpretative Report (2.2.01.02)	Start On or After	120			03-Apr-18 A	31-Jul-18 A				100%	
05-1200	DCM Static Load Test Proposal (2.2.03)	Start On or After	224			03-Apr-18 A	13-Nov-18 A				100%	
05-1280	Draft plan of 2D/3D modelling works for seawall and breakwater design (2.2.05)	Start On or After	728	31-Mar-20	29-Apr-20	03-May-18 A	29-Apr-20	26-Nov-19	26-Dec-19	-126	80%	
05-2930	Reclamation design (2.2.07)	Start On or After	91			03-Aug-18 A	02-Nov-18 A				100%	
05-2940	Seawall design (2.2.08)	Start On or After	323			11-Apr-18 A	28-Feb-19 A				100%	
05-2950	Breakwater design (2.2.09)	Start On or After	293			02-May-18 A	19-Feb-19 A				100%	
05-2960	Berth design (2.2.10)	Start On or After	342			11-Apr-18 A	19-Mar-19 A				70%	
05-2970	Onshore crane Facility (2.2.11)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	07-Mar-21	20-Jul-21	341	0%	
05-2980	Onshore vessel power supply system (2.2.12)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	15-Dec-19	28-Apr-20	-107	0%	
EP_SP_66_12-WP-3-M28.05.01.03	AIP Incineration Plant Buildings (2.3)		961	31-Mar-20	25-Dec-20	10-May-18 A	25-Dec-20	30-Aug-18	26-Jul-22	577		
EP_SP_66_12-WP-3-M28.05.01.03.1	Architectural Design (2.3.00)		740	31-Mar-20	12-Aug-20	04-Aug-18 A	12-Aug-20	15-Dec-20	12-Aug-21	364		
05-1210	Process Building	Start On or After	605	31-Mar-20	29-May-20	03-Oct-18 A	29-May-20	15-Dec-20	13-Feb-21	259	65%	
05-1220	ACC Equipment Structure	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	16-Feb-21	01-Jul-21	322	0%	
05-1230	Turbine Hall Building	Start On or After	410			30-Aug-18 A	14-Oct-19 A				100%	
05-1240	Air Compressor Building	Start On or After	433			30-Aug-18 A	06-Nov-19 A				100%	
05-1250	Chimney and viewing platform	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	28-Jan-21	12-Jun-21	303	0%	
05-1260	Elevated Drive Way and Associated Structures	Start On or After	464			04-Aug-18 A	11-Nov-19 A				100%	
05-1270	Reception Pavilion	Start On or After	665	31-Mar-20	29-May-20	04-Aug-18 A	29-May-20	13-Jun-21	12-Aug-21	439	65%	
EP_SP_66_12-WP-3-M28.05.01.03.2	Foundation design (2.3.01)		252	31-Mar-20	31-Mar-20	23-Jul-19 A	31-Mar-20	02-Jul-21	19-Jun-22	810		
05-3030	Process Building (2 Packages)	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20*	31-Mar-20	02-Jul-21	02-Jul-21	458	0%	
05-3040	ACC Equipment Structure	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20*	31-Mar-20	18-Oct-21	18-Oct-21	566	0%	
05-3050	Turbine Hall Building	Start On or After	59			23-Jul-19 A	20-Sep-19 A				100%	
05-3060	Air Compressor Building	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20*	31-Mar-20	27-Jan-22	27-Jan-22	667	0%	
05-3070	Chimney and viewing platform	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20*	31-Mar-20	29-Sep-21	29-Sep-21	547	0%	
05-3080	Elevated Drive Way and Associated Structures Foundation Design	Start On or After	77	31-Mar-20	31-Mar-20	14-Jan-20 A	31-Mar-20	06-Feb-22	06-Feb-22	677	45%	
05-3090	Reception Pavilion	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20*	31-Mar-20	19-Jun-22	19-Jun-22	810	0%	
EP_SP_66_12-WP-3-M28.05.01.03.3	Structural design (2.3.02)		487	31-Mar-20	31-Mar-20	30-Nov-18 A	31-Mar-20	14-Nov-20	26-Jul-22	847		
05-1290	Process Building	Start On or After	386	31-Mar-20	31-Mar-20	11-Mar-19 A	31-Mar-20	20-Sep-21	20-Sep-21	538	5%	
05-1300	ACC Equipment Structure	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20*	31-Mar-20	14-Nov-20	14-Nov-20	228	0%	
05-1310	Turbine Hall Building	Start On or After	154			30-Nov-18 A	03-May-19 A				100%	
05-1320	Air Compressor Building	Start On or After	98			14-Jun-19 A	20-Sep-19 A				100%	
05-1330	Chimney	Start On or After	305	31-Mar-20	31-Mar-20	31-May-19 A	31-Mar-20	26-Jul-22	26-Jul-22	847	5%	
05-1340	Access Ramp associated structures	Start On or After	237			19-Mar-19 A	11-Nov-19 A				100%	
05-1350	Reception Pavilion Structural Design	Start On or After	101			29-Jul-19 A	07-Nov-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.03.4	Electrical and Instrumentation works design (2.3.03)		456			10-May-18 A	09-Aug-19 A					
05-3150	11kV/380V Power Transformers and 11kV Earthing Transformer	Start On or After	315			06-Sep-18 A	18-Jul-19 A				100%	
05-3160	E&I Package 1 (Process Island)	Start On or After	391			10-May-18 A	05-Jun-19 A				100%	
05-3170	E&I Package 2 (Power Island)	Start On or After	288			25-Oct-18 A	09-Aug-19 A				100%	
05-3175(3)(M12)	E&I Package 3 (Balance of Plant)	Start On or After	288			25-Oct-18 A	09-Aug-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.03.8	Operation Management System (2.3.03.04)		721	31-Mar-20	29-Apr-20	10-May-18 A	29-Apr-20	28-Apr-20	10-Sep-20	133		
05-3180	Supervisory Control/Data Acquisition/Distributed Control (SCADA/DCS) System	Start On or After	721	31-Mar-20	29-Apr-20	10-May-18 A	29-Apr-20	28-Apr-20	28-May-20	28	65%	
05-3210	Automatic License Plate and Container Recognition System (ALPCRS)	Start On or After	603	31-Mar-20	29-Apr-20	05-Sep-18 A	29-Apr-20	11-Aug-20	10-Sep-20	133	65%	
EP_SP_66_12-WP-3-M28.05.01.03.5	Mechanical works design (2.3.04)		433			17-May-18 A	24-Jul-19 A					
EP_SP_66_12-WP-3-M28.05.01.03.5.1	Plant and Equipment		419			31-May-18 A	24-Jul-19 A					
05-2800	Weighbridge Systems	Start On or After	152			05-Sep-18 A	04-Feb-19 A				100%	
05-2810	Waste Crane and Grapple System	Start On or After	221			05-Jul-18 A	11-Feb-19 A				100%	
05-2820	Mechanical Shredder	Start On or After	243			23-Nov-18 A	24-Jul-19 A				100%	
05-2830	Incineration System	Start On or After	165			31-May-18 A	12-Nov-18 A				100%	
05-2840	Heat Recovery Boiler	Start On or After	145			08-Jun-18 A	31-Oct-18 A				100%	
05-2850	Boiler Feed Water Systems	Start On or After	68			05-Sep-18 A	12-Nov-18 A				100%	
05-2860	Ash cranes	Start On or After	136			24-Dec-18 A	09-May-19 A				100%	
05-2870	Leachate collection and treatment	Start On or After	73			15-Dec-18 A	26-Feb-19 A				100%	
05-2880	Flue Gas Treatment System	Start On or After	184			11-Jun-18 A	12-Dec-18 A				100%	
05-2890	Boiler ash and APC residue handling and solidification	Start On or After	100			24-Dec-18 A	03-Apr-19 A				100%	
05-2900	Steam Turbine Generator (STG) and Pressure Reducing and Desuperheating Station (PRDS)	Start On or After	325			03-Aug-18 A	24-Jun-19 A				100%	
05-2910	Air cooled condenser	Start On or After	325			03-Aug-18 A	24-Jun-19 A				100%	
05-2915(3)	Closed Circuit Cooling Water System	Start On or After	321			31-Jul-18 A	17-Jun-19 A				100%	
05-2920	Compressed Air Plants	Start On or After	232			04-Jul-18 A	21-Feb-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.03.5.2	Process Pipeworks (Incl. Ductworks) and Valves		404			24-May-18 A	02-Jul-19 A					
05-1360	Process Island (furnace-boiler-FGC)	Start On or After	224			24-May-18 A	03-Jan-19 A				100%	

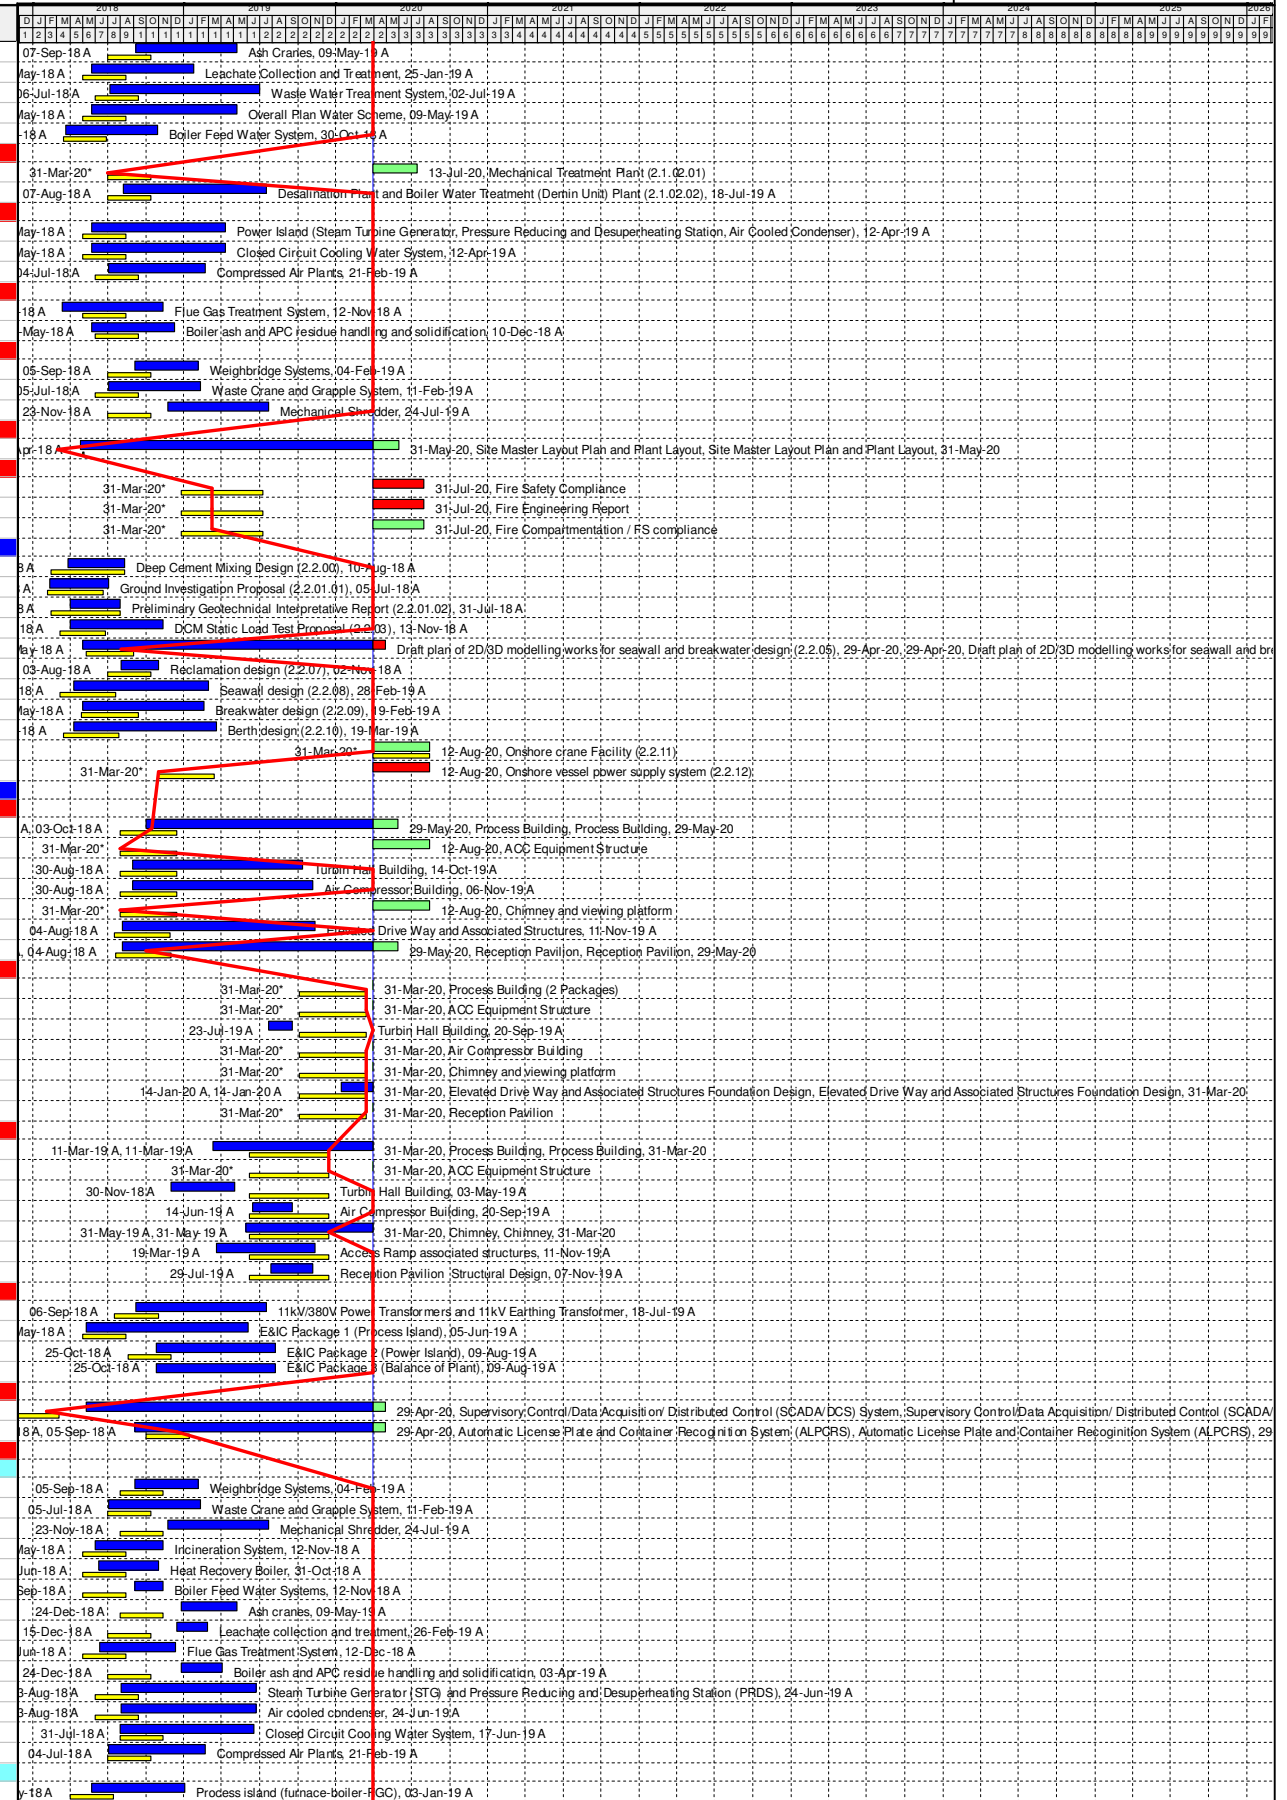

Programme for Design and Construction Works
 March 2020 Update (Rev WP-3-M28)

Primary Baseline	Critical Remaining Work	Actual Milestone
WP3 BL Critical Works	Baseline Milestone	Critical Milestone
Remaining Work	WP3 BL Critical Milestone	
Actual Work	Milestone	

Date	Revision	Checked	Approved

Activity ID	Activity Name	Primary Constraint	At Completion Duration	Current Start	Current Finish	Actual Start	Actual Finish	Latest Start	Latest Finish	Total Float	Activity % Complete	M28 Remarks
05-1370	Pipebridge (Between Process Island & Turbine Hall)	Start On or After	404			24-May-18 A	02-Jul-19 A				100%	
05-1380	Compressed Air Plant area	Start On or After	273			02-Oct-18 A	02-Jul-19 A				100%	
05-1390	Pipebridge (Between CCGW Area & Turbine Hall)	Start On or After	119			02-Oct-18 A	29-Jan-19 A				100%	
05-1400	Pipebridge (Between Turbine Hall & ACC Yard)	Start On or After	119			02-Oct-18 A	29-Jan-19 A				100%	
05-1410	Turbine Hall	Start On or After	273			02-Oct-18 A	02-Jul-19 A				100%	
05-1420	ACC Yard	Start On or After	273			02-Oct-18 A	02-Jul-19 A				100%	
05-1540	CCGW Area	Start On or After	273			02-Oct-18 A	02-Jul-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.03.5.3 Process steel structure support (For equipment, piping & duct, cable tray etc)												
05-3100	Process island (furnace-boiler-FGC)	Start On or After	246			17-May-18 A	29-Jan-19 A				100%	
05-3110	Pipebridge (Between Process Island & Turbine Hall)	Start On or After	112			09-Oct-18 A	29-Jan-19 A				100%	
05-3120	Turbine Hall	Start On or After	112			09-Oct-18 A	29-Jan-19 A				100%	
05-3130	Pipebridge (Between CCGW Area & Turbine Hall)	Start On or After	112			09-Oct-18 A	29-Jan-19 A				100%	
05-3140	Pipebridge (Between Turbine Hall & ACC Yard)	Start On or After	112			09-Oct-18 A	29-Jan-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.03.5.4 Equipment and piping insulation												
05-1430	Incineration System	Start On or After	150			15-Jun-18 A	12-Nov-18 A				100%	
05-1440	Heat Recovery Boiler	Start On or After	138			15-Jun-18 A	31-Oct-18 A				100%	
05-1450	Boiler Feed Water Systems	Start On or After	150			15-Jun-18 A	12-Nov-18 A				100%	
05-1460	Flue Gas Treatment System	Start On or After	180			15-Jun-18 A	12-Dec-18 A				100%	
05-1470	Boiler ash and APC residue handling and solidification	Start On or After	292			15-Jun-18 A	03-Apr-19 A				100%	
05-1480	Steam Turbine Generator (STG) and Pressure Reducing and Desuperheating Station (PRDS)	Start On or After	181			11-Jan-19 A	11-Jul-19 A				100%	
05-1490	Air cooled condenser	Start On or After	251			02-Nov-18 A	11-Jul-19 A				100%	
05-1500	Closed Circuit Cooling Water System	Start On or After	321			31-Jul-18 A	17-Jun-19 A				100%	
EP_SP_66_12-WP-3-M28.05.01.03.6 Fire services installation design (2.3.05)												
EP_SP_66_12-WP-3-M28.05.01.03.6.1 Process Building (2.3.05.01)												
05-1510	Fire Systems	Finish On or Before	626	31-Mar-20	26-Sep-20	10-Jan-19 A	26-Sep-20	10-Apr-19	07-Oct-19	-355	5%	
05-1520	Fire engineering	Finish On or Before	569	01-Aug-20	01-Aug-20	10-Jan-19 A	01-Aug-20	07-Oct-19	07-Oct-19	-298	0%	
05-1530	FS schematics	Finish On or Before	180	31-Mar-20	26-Sep-20	10-Jan-19 A	26-Sep-20	10-Apr-19	06-Oct-19	-356	0%	
EP_SP_66_12-WP-3-M28.05.01.03.6.2 Turbin Hall Building (2.3.05.03)												
05-5400	Fire Systems (2.3.05.03.01)	Finish On or Before	453	31-Mar-20	06-Apr-20	10-Jan-19 A	06-Apr-20	01-Oct-19	07-Oct-19	-182	5%	
05-5410 (M22)	Fire engineering	Finish On or Before	729	31-Mar-20	25-Dec-20	28-Dec-18 A	25-Dec-20	17-Apr-19	11-Jan-20	-349	0%	
05-5420 (M22)	FS schematics (2.3.05.03.03)	Finish On or Before	564	31-Mar-20	13-Jul-20	28-Dec-18 A	13-Jul-20	22-Jun-19	04-Oct-19	-283	25%	
EP_SP_66_12-WP-3-M28.05.01.03.6.4 Air Compressor Building (2.3.05.04)												
05-5430 (M22)	Fire Systems	Finish On or Before	270	31-Mar-20	25-Dec-20	31-Mar-20	25-Dec-20	30-Aug-18	26-May-19	-579	0%	
05-5440 (M22)	FS schematics	Finish On or Before	270	31-Mar-20	25-Dec-20	31-Mar-20	25-Dec-20	30-Aug-18	26-May-19	-579	0%	
EP_SP_66_12-WP-3-M28.05.01.03.6.5 Elevated Drive Way and Associated Structures (2.3.05.05)												
05-5445 (M22)	Fire Systems	Finish On or Before	255	31-Mar-20	26-Aug-20	16-Dec-19 A	26-Aug-20	29-Oct-19	25-Mar-20	-154	5%	
05-5450 (M22)	FS schematics	Finish On or Before	255	31-Mar-20	26-Aug-20	16-Dec-19 A	26-Aug-20	29-Oct-19	25-Mar-20	-154	5%	
EP_SP_66_12-WP-3-M28.05.01.03.6.6 Reception Pavilion (2.3.05.06)												
05-5460 (M22)	Fire Systems (2.3.05.06.01)	Finish On or Before	357	31-Mar-20	24-Sep-20	04-Oct-19 A	24-Sep-20	16-Dec-19	10-Jun-20	-106	5%	
05-5470 (M22)	FS schematics (2.3.05.06.03)	Finish On or Before	356	31-Mar-20	23-Sep-20	04-Oct-19 A	23-Sep-20	17-Dec-19	10-Jun-20	-105	5%	
EP_SP_66_12-WP-3-M28.05.01.03.6.7 Compressor & Closed Circuit (2.3.05.07)												
05-5480 (M22)	Fire Systems (2.3.05.07.01)	Finish On or Before	307	31-Mar-20	13-Jul-20	11-Sep-19 A	13-Jul-20	13-Oct-19	25-Jan-20	-170	45%	
05-5490 (M22)	FS schematics (2.3.05.07.03)	Finish On or Before	307	31-Mar-20	13-Jul-20	11-Sep-19 A	13-Jul-20	13-Oct-19	25-Jan-20	-170	45%	
EP_SP_66_12-WP-3-M28.05.01.03.7 Building services design (excluding fire services installation design) (2.3.05)												
05-1550	Electrical Services and Lighting (7 Packages)	Start On or After	764	31-Mar-20	12-Aug-20	11-Jul-18 A	12-Aug-20	19-May-20	29-Apr-21	259	12.5%	
05-1560	MVAC (6 Packages)	Start On or After	577	31-Mar-20	09-Aug-20	10-Jan-19 A	09-Aug-20	23-Jul-20	02-Dec-20	115	5%	
05-1570	Odour Control	Start On or After	476	31-Mar-20	29-Apr-20	10-Jan-19 A	29-Apr-20	12-Oct-20	11-Nov-20	195	5%	
05-1580	Plumbing (7 Packages)	Start On or After	719	31-Mar-20	28-Jun-20	11-Jul-18 A	28-Jun-20	13-Aug-20	11-Nov-20	135	5%	
05-1590	Drainage (7 Packages)	Start On or After	441	31-Mar-20	31-Mar-20	15-Jan-19 A	31-Mar-20	16-Nov-20	16-Nov-20	230	5%	
05-1600	ELV (7 Packages)	Start On or After	531	31-Mar-20	28-Jun-20	15-Jan-19 A	28-Jun-20	18-Aug-20	16-Nov-20	140	5%	
05-1610	Lifts and Escalators (2 Packages)	Start On or After	536	31-Mar-20	28-Jun-20	10-Jan-19 A	28-Jun-20	17-Nov-20	15-Feb-21	231	5%	
05-1630	Building Management System (BMS) (7 Packages)	Start On or After	227	31-Mar-20	12-Aug-20	30-Dec-19 A	12-Aug-20	04-Jun-20	17-Oct-20	65	5%	
05-1770	Vehicle & Container Wash System	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20	12-Aug-20	19-May-20	30-Sep-20	49	0%	
05-1770-1(M20)	Water Cannon System	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20	12-Aug-20	01-Oct-20	13-Feb-21	184	0%	
05-1770-1(M20)	Water Cannon System	Start On or After	294	31-Mar-20	31-Mar-20	11-Jun-19 A	31-Mar-20	29-Apr-21	29-Apr-21	394	5%	
EP_SP_66_12-WP-3-M28.05.01.04 AIP Mechanical Treatment Plant Building (2.4)												
05-1640	Architectural Design (2.4.00)	Start On or After	706	31-Mar-20	12-Aug-20	07-Sep-18 A	12-Aug-20	19-Nov-19	25-Oct-21	438	65%	
05-1650	Foundation design (2.4.01)	Start On or After	631	31-Mar-20	29-May-20	07-Sep-18 A	29-May-20	22-Nov-20	21-Jan-21	236	65%	
05-1660	Structural design (2.4.02)	Start On or After	268	31-Mar-20	31-Mar-20	07-Jul-19 A	31-Mar-20	25-Oct-21	25-Oct-21	573	65%	
05-1670	Electrical and instrumentation works design (2.4.03)	Start On or After	206	31-Mar-20	13-Jul-20	21-May-19 A	13-Dec-19 A			100%	100%	
05-1680	Mechanical works design (2.4.04)	Start On or After	105	31-Mar-20	13-Jul-20	31-Mar-20	13-Jul-20	14-Jul-20	27-Oct-20	105	0%	
05-1690	Fire services installation design (2.4.05) (3 Packages)	Start On or After	105	31-Mar-20	13-Jul-20	31-Mar-20	13-Jul-20	19-Nov-19	03-Mar-20	-133	0%	
05-1690	Fire services installation design (2.4.05) (3 Packages)	Start On or After	472	31-Mar-20	04-Jul-20	20-Mar-19 A	04-Jul-20	31-Jan-21	06-May-21	306	9.5%	
EP_SP_66_12-WP-3-M28.05.01.04.7 Building services design (excluding fire services installation design) (2.4.06)												
05-1700	Electrical Services and Lighting (2.4.06.01)	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	15-Apr-20	15-May-21	275	5%	
05-1710	MVAC	Start On or After	377	31-Mar-20	31-Mar-20	20-Mar-19 A	31-Mar-20	02-Dec-20	02-Dec-20	246	5%	
05-1720	Odour Control	Start On or After	507	31-Mar-20	12-Aug-20	25-Mar-19 A	12-Aug-20	15-Apr-20	28-Aug-20	15	5%	
05-1730	Plumbing	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20	12-Aug-20	15-Apr-20	28-Aug-20	15	0%	
05-1740	Drainage	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	04-Jul-20	16-Nov-20	95	5%	
05-1750	ELV	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	04-Jul-20	16-Nov-20	95	5%	
05-1760	Lifts and Escalators	Start On or After	227	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	20-Jul-20	02-Dec-20	111	5%	
05-1760-1(M20)	Building Management System (BMS)	Start On or After	227	31-Mar-20	12-Aug-20	30-Dec-19 A	12-Aug-20	31-Dec-20	15-May-21	275	5%	
05-1760-1(M20)	Building Management System (BMS)	Start On or After	89	31-Mar-20	27-Jun-20	31-Mar-20	27-Jun-20	04-Jul-20	30-Sep-20	95	0%	
EP_SP_66_12-WP-3-M28.05.01.05 AIP Wastewater Treatment Plant (2.5)												
05-1780	Architectural Design (2.5.00)	Start On or After	715	31-Mar-20	16-Sep-20	03-Oct-18 A	16-Sep-20	15-Apr-20	04-Jul-21	230	65%	
05-1790	Foundation design (2.5.01)	Start On or After	605	31-Mar-20	29-May-20	03-Oct-18 A	29-May-20	26-Dec-20	24-Feb-21	270	65%	
05-1800	Structural design (2.5.02)	Start On or After	0	31-Mar-20	31-Mar-20	31-Mar-20	31-Mar-20	04-Jul-21	04-Jul-21	460	0%	
05-1810	Electrical and instrumentation works design (2.5.03)	Start On or After	556	31-Mar-20	16-Sep-20	11-Mar-19 A	16-Sep-20	30-May-20	16-Nov-20	60	45%	
05-1820	Mechanical works design (2.5.04)	Start On or After	289	31-Mar-20	16-Sep-20	24-Oct-18 A	09-Aug-19 A			100%	100%	
05-2790	Fire services installation design (2.5.05)	Start On or After	282	31-Mar-20	12-Jul-19 A	03-Oct-18 A	12-Jul-19 A			100%	100%	
05-2790	Fire services installation design (2.5.05)	Start On or After	530	31-Mar-20	28-Jun-20	16-Jan-19 A	28-Jun-20	05-Feb-21	06-May-21	311	5%	
EP_SP_66_12-WP-3-M28.05.01.05.7 Building services design (excluding fire services installation design) (2.5.06)												
05-1830	Electrical Services and Lighting for Wastewater Treatment Plant Building (2.5.06.01)	Start On or After	575	31-Mar-20	12-Aug-20	16-Jan-19 A	12-Aug-20	15-Apr-20	02-Dec-20	111	5%	
05-1840	MVAC (2.5.06.02)	Start On or After	470	31-Mar-20	29-Apr-20	16-Jan-19 A	29-Apr-20	02-Nov-20	02-Dec-20	216	25%	
05-1850	Odour Control (2.5.06.03)	Start On or After	560	31-Mar-20	28-Jul-20	16-Jan-19 A	28-Jul-20	30-Apr-20	28-Aug-20	30	25%	
05-1860	Plumbing (2.5.06.04)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20	12-Aug-20	15-Apr-20	28-Aug-20	15	0%	
05-1870	Drainage (2.5.06.05)	Start On or After	560	31-Mar-20	28-Jul-20	16-Jan-19 A	28-Jul-20	19-Jul-20	16-Nov-20	110	25%	
05-1880	ELV (2.5.06.06)	Start On or After	560	31-Mar-20	28-Jul-20	16-Jan-19 A	28-Jul-20	04-Aug-20	02-Dec-20	126	25%	
EP_SP_66_12-WP-3-M28.05.01.06 AIP Desalination Plant Building (2.6)												
05-1900	Architectural Design (2.6.00)	Start On or After	706	31-Mar-20	12-Aug-20	07-Sep-18 A	12-Aug-20	15-Apr-20	25-Sep-21	408	65%	
05-1910	Foundation design (2.6.01)	Start On or After	631	31-Mar-20	29-May-20	07-Sep-18 A	29-May-20	22-Nov-20	21-Jan-21	236	65%	

Programme for Design and Construction Works
March 2020 Update (Rev WP-3-M28)
 Page 4 of 23

Primary Baseline	Critical Remaining Work	Actual Milestone
WP3 BL Critical Works	Baseline Milestone	Critical Milestone
Remaining Work	WP3 BL Critical Milestone	
Actual Work	Milestone	

Date	Revision	Checked	Approved
04/12/17	Rev. 0 - 1st Issue		
31-Jan-20	Rev 3 - Jan		

Activity ID	Activity Name	Primary Constraint	At Completion Duration	Current Start	Current Finish	Actual Start	Actual Finish	Latest Start	Latest Finish	Total Float	Activity % Complete	M28 Remarks
05-1920	Structural design (2.6.02)	Start On or After	206			21-May-19 A	13-Dec-19 A				100%	
05-1930	Electrical and instrumentation works design (2.6.03)	Start On or After	289			24-Oct-18 A	09-Aug-19 A				100%	
05-1940	Mechanical works design (2.6.04)	Start On or After	195			30-Nov-18 A	13-Jun-19 A				100%	
05-1950	Fire services installation design (2.6.05) (3 Packages)	Start On or After	462	31-Mar-20	24-Jun-20	20-Mar-19 A	24-Jun-20	09-Feb-21	06-May-21	316	19%	
EP_SP_66_12-WP-3-M28.05.01.06.7 Building services design (excluding fire services installation design) (2.6.06)												
05-1960	Electrical Services and Lighting (2.6.06.01)	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	15-Apr-20	02-Dec-20	111	5%	
05-1970	MVAC	Start On or After	507	31-Mar-20	12-Aug-20	25-Mar-19 A	12-Aug-20	15-Apr-20	28-Aug-20	15	5%	
05-1980	Odour Control	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	15-Apr-20	28-Aug-20	15	0%	
05-1990	Plumbing	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	04-Jul-20	16-Nov-20	95	5%	
05-2000	Drainage	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	04-Jul-20	16-Nov-20	95	5%	
05-2010	ELV	Start On or After	512	31-Mar-20	12-Aug-20	20-Mar-19 A	12-Aug-20	20-Jul-20	02-Dec-20	111	5%	
EP_SP_66_12-WP-3-M28.05.01.07 AIP Administration Building (2.7)												
05-2020	Architectural Design (2.7.00)	Start On or After	666	31-Mar-20	29-May-20	03-Aug-18 A	29-May-20	23-Oct-20	22-Dec-20	206	65%	
05-2030	Foundation design (2.7.01)	Start On or After	142			30-Sep-19 A	19-Feb-20 A				100%	
05-2040	Structural design (2.7.02)	Start On or After	446	31-Mar-20	16-Oct-20	29-Jul-19 A	16-Oct-20	09-Oct-21	27-Apr-22	557	65%	
05-2050	Electrical and instrumentation works design (2.7.03)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	04-Oct-20	16-Feb-21	187	0%	
05-2060	Fire services installation design (3 Packages) (2.7.04)	Start On or After	332	31-Mar-20	31-Jul-20	03-Sep-19 A	31-Jul-20	04-Dec-20	06-Apr-21	249	9.5%	
EP_SP_66_12-WP-3-M28.05.01.07.6 Building services design (excluding fire services installation design) (2.7.05)												
05-2070	Electrical Services and Lighting (2.7.05.01)	Start On or After	345	31-Mar-20	12-Aug-20	03-Sep-19 A	12-Aug-20	15-Apr-20	02-Dec-20	111	5%	
05-2080	MVAC	Start On or After	345	31-Mar-20	12-Aug-20	03-Sep-19 A	12-Aug-20	15-Apr-20	28-Aug-20	15	5%	
05-2090	Odour Control	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	15-Apr-20	28-Aug-20	15	0%	
05-2100	Plumbing	Start On or After	345	31-Mar-20	12-Aug-20	03-Sep-19 A	12-Aug-20	04-Jul-20	16-Nov-20	95	5%	
05-2110	Drainage	Start On or After	345	31-Mar-20	12-Aug-20	03-Sep-19 A	12-Aug-20	04-Jul-20	16-Nov-20	95	5%	
05-2120	ELV	Start On or After	345	31-Mar-20	12-Aug-20	03-Sep-19 A	12-Aug-20	20-Jul-20	02-Dec-20	111	5%	
05-2130	Lifts and Escalators	Start On or After	227	31-Mar-20	12-Aug-20	30-Dec-19 A	12-Aug-20	04-Jun-20	17-Oct-20	65	5%	
05-2130-1(M20)	Building Management System (BMS)	Start On or After	89	31-Mar-20	27-Jun-20	31-Mar-20*	27-Jun-20	04-Jul-20	30-Sep-20	95	0%	
EP_SP_66_12-WP-3-M28.05.01.08 AIP IWMF Substation (2.8)												
05-2140	Architectural Design (2.8.00)	Start On or After	437			03-Aug-18 A	14-Oct-19 A				100%	
05-2150	Foundation design (2.8.01)	Start On or After	124			17-May-19 A	18-Sep-19 A				100%	
05-2160	Structural design (2.8.02)	Start On or After	168			31-Oct-18 A	17-Apr-19 A				100%	
05-2170	Electrical and instrumentation works design (2.8.03) (14 Packages)	Start On or After	245	31-Mar-20	25-Jun-20	25-Oct-19 A	25-Jun-20	02-Jul-20	27-Sep-20	93	51.67%	
05-2180	Mechanical works design (2.8.04)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	01-Mar-20	14-Jul-20	-30	0%	
05-2190	Fire services installation design (2.8.05) (2 Packages)	Start On or After	612	31-Mar-20	30-Jul-20	27-Nov-18 A	30-Jul-20	21-Sep-20	21-Jan-21	174	28.5%	
EP_SP_66_12-WP-3-M28.05.01.08.7 Building services design (excluding fire services installation design) (2.8.06)												
05-2200	Electrical Services and Lighting (2.8.06.01)	Start On or After	591	31-Mar-20	09-Jul-20	27-Nov-18 A	09-Jul-20	19-May-20	02-Dec-20	145	36%	
05-2210	MVAC	Start On or After	576	31-Mar-20	25-Jun-20	27-Nov-18 A	25-Jun-20	06-Sep-20	02-Dec-20	160	36%	
05-2220	Plumbing	Start On or After	591	31-Mar-20	09-Jul-20	27-Nov-18 A	09-Jul-20	07-Aug-20	16-Nov-20	129	65%	
05-2230	Drainage	Start On or After	387	31-Mar-20	28-Jun-20	27-Nov-18 A	28-Jun-20	03-Sep-20	02-Dec-20	156	65%	
05-2240	ELV	Start On or After	580	31-Mar-20	28-Jun-20	27-Nov-18 A	28-Jun-20	03-Sep-20	02-Dec-20	156	65%	
05-2240-1(M20)	Building Management System (BMS)	Start On or After	89	31-Mar-20	27-Jun-20	31-Mar-20*	27-Jun-20	03-Jul-20	29-Sep-20	94	0%	
EP_SP_66_12-WP-3-M28.05.01.09 AIP Air Quality Monitoring Stations (2.9)												
05-2250	Design of the Air Quality Monitoring Stations (2.9.01)	Start On or After	120	31-Mar-20	28-Jul-20	31-Mar-20*	28-Jul-20	06-Jul-20	03-Nov-20	97	0%	
EP_SP_66_12-WP-3-M28.05.01.10 AIP Roads and Utilities (2.10)												
EP_SP_66_12-WP-3-M28.05.01.10.1 Permanent road works layout on the Artificial Island (2.10.01)												
05-2260	Roads and hardstandings layout	Start On or After	135	17-Dec-20	30-Apr-21	17-Dec-20*	30-Apr-21	26-Aug-22	07-Jun-23	767	0%	
05-2270	Road signage and markings	Start On or After	135	17-Dec-20	30-Apr-21	17-Dec-20*	30-Apr-21	23-Jan-23	07-Jun-23	767	0%	
EP_SP_66_12-WP-3-M28.05.01.10.2 Sewerage design on the Artificial Island (2.10.02)												
05-2280	Foul Sewerage concept sizing	Start On or After	330	31-Mar-20	12-Aug-20	18-Sep-19 A	12-Aug-20	03-Aug-20	30-Jan-22	535	65%	
05-2290	Contaminated Sewerage concept / sizing	Start On or After	330	31-Mar-20	12-Aug-20	18-Sep-19 A	12-Aug-20	17-Sep-21	30-Jan-22	535	65%	
EP_SP_66_12-WP-3-M28.05.01.10.3 Drainage system design on the Artificial Island (2.10.03)												
05-2300	Surface Water Drainage System concept / sizing	Start On or After	449	31-Mar-20	12-Aug-20	22-May-19 A	12-Aug-20	03-Aug-20	16-Dec-20	125	65%	
05-2310	First Flush Drainage System concept / sizing	Start On or After	449	31-Mar-20	12-Aug-20	22-May-19 A	12-Aug-20	21-Nov-20	05-Apr-21	235	65%	
EP_SP_66_12-WP-3-M28.05.01.10.4 Water supply system design on the Artificial Island (2.10.04)												
05-2320	Potable Water Distribution System (2.10.04.01)	Start On or After	349	31-Mar-20	12-Aug-20	30-Aug-19 A	12-Aug-20	30-Nov-19	01-Mar-22	565	5%	
05-2330	Recycled Water System (2.10.04.02)	Start On or After	272	31-Mar-20	12-Aug-20	14-Nov-19 A	12-Aug-20	28-Aug-21	10-Jan-22	515	5%	
05-2340	Irrigation System (2 Packages) (2.10.04.03)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	03-Aug-20	16-Dec-20	125	0%	
05-2350	Rainwater harvesting System (2.10.04.04)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	03-Aug-20	16-Dec-20	125	0%	
05-2360	Water Tanks (2.10.04.05)	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	17-Oct-21	01-Mar-22	565	0%	
05-2370	External FS Systems (2.10.04.06)	Start On or After	283	31-Mar-20	12-Aug-20	04-Nov-19 A	12-Aug-20	17-Oct-21	01-Mar-22	565	5%	
05-2370-1(M24)	E&M system for seawater intake and brine discharge (2.10.04.07)	Finish On or Before	307	31-Mar-20	01-Jul-20	30-Aug-19 A	01-Jul-20*	30-Nov-19	01-Mar-20	-122	5%	
05-2370-2(M24)	Building Services system for seawater intake and brine discharge (2.10.04.09)	Finish On or Before	88	31-Mar-20	26-Jun-20	31-Mar-20	26-Jun-20*	30-Nov-19	25-Feb-20	-122	0%	
EP_SP_66_12-WP-3-M28.05.01.10.6 Design of telecommunication and other utilities (2.10.06)												
05-2380	Power Distribution System concept / schematics	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	31-Dec-20	15-May-21	275	0%	
05-2390	Site Lighting Concept / Schematics	Start On or After	239	31-Mar-20	12-Aug-20	18-Dec-19 A	12-Aug-20	26-Jan-20	09-Jun-20	-65	5%	
05-2400	Lightning Protection System concept / schematics	Start On or After	239	31-Mar-20	12-Aug-20	18-Dec-19 A	12-Aug-20	13-Aug-20	26-Dec-20	135	5%	
05-2410	Site ELV Network System - Communications System concept / schematics	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	31-Dec-20	15-May-21	275	0%	
05-2420	Site ELV Network System - Security Systems concept / schematics	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	31-Dec-20	15-May-21	275	0%	
05-2430	Site ELV Network System - Navigation aids concept / schematics	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	31-Dec-20	15-May-21	275	0%	
05-2440	Microwave transmission of FS direct link (2.10.06.07)	Start On or After	580	31-Mar-20	28-Jun-20	27-Nov-18 A	28-Jun-20	14-Feb-21	15-May-21	320	45%	
05-2450	Fuel Handling System concept / schematics (2.10.06.08)	Start On or After	202	31-Mar-20	12-Aug-20	24-Jan-20 A	12-Aug-20	10-Sep-22	23-Jan-23	893	0%	
05-3190	Computerised Maintenance Management System (CMMS)	Start On or After	380	31-Mar-20	13-Jul-20	30-Jun-19 A	13-Jul-20	28-May-20	10-Sep-20	58	0%	
05-3200	Information and Document Management System (IDMS)	Start On or After	448	31-Mar-20	13-Jul-20	23-Apr-19 A	13-Jul-20	28-May-20	10-Sep-20	58	0%	
05-3840 (M22)	Automatic Traffic Control System (ATCS)	Start On	300	31-Mar-20	24-Jan-21	31-Mar-20*	24-Jan-21	18-Dec-19	12-Oct-20	-104	0%	
EP_SP_66_12-WP-3-M28.05.01.10.7 Utility ducts/Pipebridges design (2.10.25)												
05-2460	Design of Pipe / Utilities Trenches concept	Start On or After	135	30-May-21	11-Oct-21	30-May-21*	11-Oct-21	19-Dec-22	03-May-23	568	0%	
05-2470	Utility ducts network	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	19-Apr-20	01-Sep-20	19	0%	
05-2480	Pipebridge network - Layout	Start On or After	120	31-Mar-20	28-Jul-20	31-Mar-20*	28-Jul-20	04-May-20	01-Sep-20	34	0%	
05-2490	Pipebridge network - Foundation Plan	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	19-Apr-20	01-Sep-20	19	0%	
05-2500	Pipebridge network - Structure Plan	Start On or After	135	31-Mar-20	12-Aug-20	31-Mar-20*	12-Aug-20	19-Apr-20	01-Sep-20	19	0%	
EP_SP_66_12-WP-3-M28.05.01.11 AIP Architectural, Finishes and Landscaping Works (2.11)												
EP_SP_66_12-WP-3-M28.05.01.11.1 External and internal finishes design for Incineration Plant Buildings (2.11.01)												
05-2510	External and internal finishes design for Incineration Plant Building (6 Packages)	Start On or After	137	31-Mar-20	14-Aug-20	31-Mar-20*	14-Aug-20	28-Jun-21	12-Nov-21	454	0%	
05-2520	External and internal finishes design for ACC Equipment Structure	Start On or After	137	31-Mar-20	14-Aug-20	31-Mar-20*	14-Aug-20	28-Jun-21	12-Nov-21	454	0%	
05-2530	External and internal finishes design for Turbine Hall Building (3 Packages)	Start On or After	137	31-Mar-20	14-Aug-20	31-Mar-20*	14-Aug-20	26-Sep-21	10-Feb-22	544	0%	
05-2540	External and internal finishes design for Air Compressor Building (3 Packages)	Start On or After	137	31-Mar-20	14-Aug-20	31-Mar-20*	14-Aug-20	24-Aug-21	08-Jan-22	511	0%	
05-2550	External and internal finishes design for Chimney (6 Packages)	Start On or After	137	31-Mar-20	14-Aug-20	31-Mar-20*	14-Aug-20	27-Aug-21	11-Jan-22	514	0%	
05-2560	External and internal finishes design for Reception Pavilion (5 Packages)	Start On or After	137	31-Mar-20	14-Aug-20	31-Mar-20*	14-Aug-20	27-Aug-21	11-Jan-22	514	0%	
EP_SP_66_12-WP-3-M28.05.01.11.2 External and internal finishes design for MT Plant Building (2.11.02)												
05-2570	External and internal finishes design for MT Plant Building (2.11.02)	Start On or After	136	31-Mar-20	13-Aug-20	31-Mar-20	13-Aug-20	13-Jun-21	27-Oct-21	439	0%	

Date	Revision	Checked	Approved
04/12/17	Rev. 0 - 1st Issue		
31-Jan-20	Rev 3 - Jan 2020 Update		
29-Feb-20	Rev 3 - Feb 2020 Update		
30-Mar-20	Rev 3 - Mar 2020 Update		

Programme for Design and Construction Works

March 2020 Update (Rev WP-3-M28)

Activity ID	Activity Name	Primary Constraint	At Completion Duration	Current Start	Current Finish	Actual Start	Actual Finish	Latest Start	Latest Finish	Total Float	Activity % Complete	M28 Remarks
07-2720(1)	IEC review and comment of Coral Monitoring Plan		4			21-Apr-18 A	25-Apr-18 A				100%	21-Apr-18 A IEC review and comment of Coral Monitoring Plan, 25-Apr-18 A
07-2730(1)	AFCD Review and approval of Coral Monitoring Plan		11			14-May-18 A	25-May-18 A				100%	14-May-18 A AFCD Review and approval of Coral Monitoring Plan, 25-May-18 A
07-2740(1)	Submission to EPD-EAD Coral Monitoring Plan		0			28-May-18 A	28-May-18 A				100%	28-May-18 A Submission to EPD-EAD Coral Monitoring Plan, 28-May-18 A
EP_SP_66_12-WP-3-M28.07.5 Baseline Monitoring Information and Report												
07-2680(1)	Compilation of Final Baseline Monitoring Report		3			29-May-18 A	01-Jun-18 A				100%	29-May-18 A Compilation of Final Baseline Monitoring Report, 01-Jun-18 A
07-2690(1)	IEC review and certification of Final baseline monitoring report		5			02-Jun-18 A	07-Jun-18 A				100%	02-Jun-18 A IEC review and certification of Final baseline monitoring report, 07-Jun-18 A
07-2700(1)	Submission to EPD-EAD Final Baseline Monitoring Report		1			13-Jun-18 A	14-Jun-18 A				100%	13-Jun-18 A Submission to EPD-EAD Final Baseline Monitoring Report, 14-Jun-18 A
EP_SP_66_12-WP-3-M28.07.4 Baseline Air Quality Monitoring Works												
07-1220	Carry out baseline Air Quality monitoring at Portion 3		365	04-Jul-22	03-Jul-23	04-Jul-22	03-Jul-23	09-Oct-22	09-Oct-23		97%	04-Jul-22 03-Jul-23 Carry out baseline Air Quality monitoring at Portion 3
07-1230	Carry out baseline Air Quality monitoring at Portion 4		365	04-Jul-22	03-Jul-23	04-Jul-22	03-Jul-23	09-Oct-22	09-Oct-23		97%	04-Jul-22 03-Jul-23 Carry out baseline Air Quality monitoring at Portion 4
07-1240	Carry out baseline Air Quality monitoring at Portion 5		365	04-Jul-22	03-Jul-23	04-Jul-22	03-Jul-23	09-Oct-22	09-Oct-23		97%	04-Jul-22 03-Jul-23 Carry out baseline Air Quality monitoring at Portion 5
EP_SP_66_12-WP-3-M28.08 Maritime Works												
EP_SP_66_12-WP-3-M28.08.3 Submissions												
08-900	Submission of Particulars for DCM Works Installations	Mandatory Start	47			29-Jan-18 A	19-Dec-18 A				100%	29-Jan-18 A Submission of Particulars for DCM Works Installations, 19-Dec-18 A
08-910	Submission of Particulars for DCM Barges/Equipment	Mandatory Start	65			23-May-18 A	27-Jul-18 A				50%	23-May-18 A Submission of Particulars for DCM Barges/Equipment, 27-Jul-18 A
08-920	Submission of Lab-bench-scale testing proposal	Mandatory Start	147			01-Mar-18 A	26-Jul-18 A				100%	01-Mar-18 A Submission of Lab-bench-scale testing proposal, 26-Jul-18 A
08-930	Submission of Preconstruction site trial proposal	Mandatory Start	137			26-Mar-18 A	10-Aug-18 A				100%	26-Mar-18 A Submission of Preconstruction site trial proposal, 10-Aug-18 A
08-940	Submission of static loading test proposal		245			13-Mar-18 A	13-Nov-18 A				100%	13-Mar-18 A Submission of static loading test proposal, 13-Nov-18 A
08-950	Particulars for Construction Works Plan (CWP) for DCM Works		51			29-Oct-18 A	19-Dec-18 A				100%	29-Oct-18 A Particulars for Construction Works Plan (CWP) for DCM Works, 19-Dec-18 A
08-960	Submission of particular for DCM materials		92			26-Mar-18 A	26-Jun-18 A				100%	26-Mar-18 A Submission of particular for DCM materials, 26-Jun-18 A
08-970	Submission of Binder		92			26-Mar-18 A	26-Jun-18 A				100%	26-Mar-18 A Submission of Binder, 26-Jun-18 A
08-980	Submission of Silt Curtain System		177			29-Jan-18 A	25-Jul-18 A				100%	29-Jan-18 A Submission of Silt Curtain System, 25-Jul-18 A
EP_SP_66_12-WP-3-M28.08.1 Marine Construction												
EP_SP_66_12-WP-3-M28.08.1.1 Phase I - Construction of Perimeter Seawalls												
EP_SP_66_12-WP-3-M28.08.1.1.3 Marine Works Preparations												
08-0900	Carry out hydrographic survey		13			10-Jan-18 A	23-Jan-18 A				100%	10-Jan-18 A Carry out hydrographic survey, 23-Jan-18 A
08-1010	Mobilization of DCM Barge for Site Trial		28			14-Jun-18 A	12-Jul-18 A				100%	14-Jun-18 A Mobilization of DCM Barge for Site Trial, 12-Jul-18 A
08-1020	Mobilization of Second DCM Barge for Construction		31			14-Nov-18 A	15-Dec-18 A				100%	14-Nov-18 A Mobilization of Second DCM Barge for Construction, 15-Dec-18 A
08-1030(3)(M15)	Mobilization of Third DCM Barge for Construction	Start On or After	76			04-Apr-19 A	19-Jun-19 A				100%	04-Apr-19 A Mobilization of Third DCM Barge for Construction, 19-Jun-19 A
08-1340(2)	Sediment Sample collection and testing Dumping Permit Application	Start On or After	30			05-Sep-18 A	05-Oct-18 A				100%	05-Sep-18 A Sediment Sample collection and testing Dumping Permit Application, 05-Oct-18 A
EP_SP_66_12-WP-3-M28.08.1.1.3.2 Marine Ground Investigation Works												
08-1005-1	Ground Investigation - CPT for DCM Design Verification (145 nr.) (Deleted 26 nrs adj, Shek Kwu Chau)		67			09-Mar-18 A	15-May-18 A				100%	09-Mar-18 A Ground Investigation - CPT for DCM Design Verification (145 nr.) (Deleted 26 nrs adj, Shek Kwu Chau), 15-May-18 A
08-1005-2	Borehole Batch 1 for DCM & Caisson Design Verification at Short Breakwater Area (5 nr. @ 1 rigs)	Start On or After	41			16-Jun-18 A	27-Jul-18 A				100%	16-Jun-18 A Borehole Batch 1 for DCM & Caisson Design Verification at Short Breakwater Area (5 nr. @ 1 rigs), 27-Jul-18 A
08-1005-3	Borehole Batch 2 for DCM & Caisson Design Verification at Seawall & Berth Area (18 nr. @ 3 rigs)	Start On or After	146			17-Apr-18 A	10-Sep-18 A				100%	17-Apr-18 A Borehole Batch 2 for DCM & Caisson Design Verification at Seawall & Berth Area (18 nr. @ 3 rigs), 10-Sep-18 A
08-1005-4	Borehole Batch 3 for Blockwork Seawall Design Verification (10 nr. @ 3 rigs)	Finish On or Before	81			27-Sep-18 A	17-Dec-18 A				100%	27-Sep-18 A Borehole Batch 3 for Blockwork Seawall Design Verification (10 nr. @ 3 rigs), 17-Dec-18 A
08-1005-5	Borehole Batch 4 for Reclamation Design (10 nr. @ 3 rigs)		140			06-Aug-18 A	24-Dec-18 A				100%	06-Aug-18 A Borehole Batch 4 for Reclamation Design (10 nr. @ 3 rigs), 24-Dec-18 A
08-1005-6	Borehole Batch 4 for DCM & Caisson Design Verification at Short Breakwater Area (8 nr. @ 1 rig)		52			31-Aug-18 A	22-Oct-18 A				100%	31-Aug-18 A Borehole Batch 4 for DCM & Caisson Design Verification at Short Breakwater Area (8 nr. @ 1 rig), 22-Oct-18 A
EP_SP_66_12-WP-3-M28.08.1.1.1 Seawall and Berth at DCM Area												
EP_SP_66_12-WP-3-M28.08.1.1.1.1 Bench-scale Testing												
08-1030-01(1)(A)	Collect Soil Sample by Vibrocore Method (16 nr.)		14			13-Mar-18 A	26-Mar-18 A				100%	13-Mar-18 A Collect Soil Sample by Vibrocore Method (16 nr.), 26-Mar-18 A
08-1030-02(1)(A)	Bench-scale Mixing		32			26-Mar-18 A	27-Apr-18 A				100%	26-Mar-18 A Bench-scale Mixing, 27-Apr-18 A
08-1030-03(1)(A)	Bench-scale Test for Trial Mix (14 days)		15			09-Apr-18 A	24-Apr-18 A				100%	09-Apr-18 A Bench-scale Test for Trial Mix (14 days), 24-Apr-18 A
08-1030-04(1)(A)	Bench-scale Test for Trial Mix (28 days)		44			23-Mar-18 A	06-May-18 A				100%	23-Mar-18 A Bench-scale Test for Trial Mix (28 days), 06-May-18 A
08-1030-05(1)(A)	Bench-scale Test for Trial Mix (90 days)		31			26-Jun-18 A	27-Jul-18 A				100%	26-Jun-18 A Bench-scale Test for Trial Mix (90 days), 27-Jul-18 A
EP_SP_66_12-WP-3-M28.08.1.1.1.2 DCM Plant & Site Trial												
08-1040-01(1)(A)	Lay Geotextile and Sand Blanket		11			09-Jul-18 A	20-Jul-18 A				100%	09-Jul-18 A Lay Geotextile and Sand Blanket, 20-Jul-18 A
08-1040-02(1)(A)	Pre CPT for Site Trial (7 nr.)	Start On or After	4			28-Jun-18 A	02-Jul-18 A				100%	28-Jun-18 A Pre CPT for Site Trial (7 nr.), 02-Jul-18 A
08-1040-03(1)(A)	DCM Plant Trial Injections - Group 1 - 3 (9 nr.)		4			23-Jul-18 A	27-Jul-18 A				100%	23-Jul-18 A DCM Plant Trial Injections - Group 1 - 3 (9 nr.), 27-Jul-18 A
08-1040-04(1)(A)	DCM Plant Trial Injections - Group 4 - 6 (9 nr.)		0			27-Jul-18 A	27-Jul-18 A				100%	27-Jul-18 A DCM Plant Trial Injections - Group 4 - 6 (9 nr.), 27-Jul-18 A
08-1040-05(1)(A)	DCM Plant Trial Injections - Group 7 (2 nr.)		0			28-Jul-18 A	28-Jul-18 A				100%	28-Jul-18 A DCM Plant Trial Injections - Group 7 (2 nr.), 28-Jul-18 A
08-1040-06(1)(A)	Coring for Proof Test - Group 1 - 3 (3 nr.)		6			19-Aug-18 A	25-Aug-18 A				100%	19-Aug-18 A Coring for Proof Test - Group 1 - 3 (3 nr.), 25-Aug-18 A
08-1040-07(1)(A)	Coring for Proof Test - Group 4 - 6 (3 nr.)		4			27-Aug-18 A	31-Aug-18 A				100%	27-Aug-18 A Coring for Proof Test - Group 4 - 6 (3 nr.), 31-Aug-18 A
08-1040-08(1)(A)	Coring for Proof Test - Group 7 (1 nr.)		2			01-Sep-18 A	02-Sep-18 A				100%	01-Sep-18 A Coring for Proof Test - Group 7 (1 nr.), 02-Sep-18 A
08-1040-09(1)(A)	Carry Laboratory Testing - Group 1 - 3 (3 nr.)		1			23-Aug-18 A	24-Aug-18 A				100%	23-Aug-18 A Carry Laboratory Testing - Group 1 - 3 (3 nr.), 24-Aug-18 A
08-1040-10(1)(A)	Carry Laboratory Testing - Group 4 - 6 (3 nr.)		1			01-Sep-18 A	01-Sep-18 A				100%	01-Sep-18 A Carry Laboratory Testing - Group 4 - 6 (3 nr.), 01-Sep-18 A
08-1040-11(1)(A)	Carry Laboratory Testing - Group 7 (1 nr.)		1			03-Sep-18 A	03-Sep-18 A				100%	03-Sep-18 A Carry Laboratory Testing - Group 7 (1 nr.), 03-Sep-18 A
EP_SP_66_12-WP-3-M28.08.1.1.2.1 Plant & Site Trial Retrial												
08-1040-13(1)(A)	Trial Injection Group 1 (2nr.)		1			11-Sep-18 A	12-Sep-18 A				100%	11-Sep-18 A Trial Injection Group 1 (2nr.), 12-Sep-18 A
08-1040-14(1)(A)	Trial Injection Group 2 (2nr.)		0			22-Sep-18 A	22-Sep-18 A				100%	22-Sep-18 A Trial Injection Group 2 (2nr.), 22-Sep-18 A
08-1040-15(1)(A)	Trial Injection Group 3 (2nr.)		0			22-Sep-18 A	22-Sep-18 A				100%	22-Sep-18 A Trial Injection Group 3 (2nr.), 22-Sep-18 A
08-1040-16(1)(A)	Trial Injection Group 4 (2nr.)		1			26-Sep-18 A	26-Sep-18 A				100%	26-Sep-18 A Trial Injection Group 4 (2nr.), 26-Sep-18 A
08-1040-17(1)(A)	Trial Injection Group 5 (2nr.)		0			26-Sep-18 A	26-Sep-18 A				100%	26-Sep-18 A Trial Injection Group 5 (2nr.), 26-Sep-18 A
08-1040-18(1)(A)	Trial Injection Group 6 (2nr.)		1			28-Sep-18 A	28-Sep-18 A				100%	28-Sep-18 A Trial Injection Group 6 (2nr.), 28-Sep-18 A
08-1040-19(1)(A)	Trial Injection Group 7 (2nr.)		1			29-Sep-18 A	29-Sep-18 A				100%	29-Sep-18 A Trial Injection Group 7 (2nr.), 29-Sep-18 A
08-1040-20(1)(A)	Trial Injection Group 8 (2nr.)		1			30-Sep-18 A	30-Sep-18 A				100%	30-Sep-18 A Trial Injection Group 8 (2nr.), 30-Sep-18 A
08-1040-21(1)(A)	Trial Injection Group 9 (2nr.)		1			01-Oct-18 A	02-Oct-18 A				100%	01-Oct-18 A Trial Injection Group 9 (2nr.), 02-Oct-18 A
08-1040-22(1)(A)	Trial Injection Group 10 (2nr.)		0			02-Oct-18 A	02-Oct-18 A				100%	02-Oct-18 A Trial Injection Group 10 (2nr.), 02-Oct-18 A
08-1040-23(1)(A)	Coring for Proof Test - No. 1 & 2		3			07-Oct-18 A	09-Oct-18 A				100%	07-Oct-18 A Coring for Proof Test - No. 1 & 2, 09-Oct-18 A
08-1040-24(1)(A)	Coring for Proof Test - No. 3 & 4		4			15-Oct-18 A	18-Oct-18 A				100%	15-Oct-18 A Coring for Proof Test - No. 3 & 4, 18-Oct-18 A
08-1040-25(1)(A)	Coring for Proof Test - No. 5 & 6		5			18-Oct-18 A	22-Oct-18 A				100%	18-Oct-18 A Coring for Proof Test - No. 5 & 6, 22-Oct-18 A
08-1040-26(1)(A)	Coring for Proof Test - No. 7 & 8		4			22-Oct-18 A	25-Oct-18 A				100%	22-Oct-18 A Coring for Proof Test - No. 7 & 8, 25-Oct-18 A
08-1040-27(1)(A)	Coring for Proof Test - No. 9		3			27-Oct-18 A	29-Oct-18 A				100%	27-Oct-18 A Coring for Proof Test - No. 9, 29-Oct-18 A
08-1040-28(1)(A)	Coring for Proof Test - No. 10 & 11		5			03-Nov-18 A	08-Nov-18 A				100%	03-Nov-18 A Coring for Proof Test - No. 10 & 11, 08-Nov-18 A
08-1040-29(1)(A)	Coring for Proof Test - No. 12 & 13		6			08-Nov-18 A	14-Nov-18 A				100%	08-Nov-18 A Coring for Proof Test - No. 12 & 13, 14-Nov-18 A
08-1040-30(1)(A)	Coring for Proof Test - No. 14 & 15		4			16-Nov-18 A	20-Nov-18 A				100%	16-Nov-18 A Coring for Proof Test - No. 14 & 15, 20-Nov-18 A
08-1040-33(1)(A)	Laboratory Testing - No. 1 & 2		0			09-Oct-18 A	09-Oct-18 A				100%	09-Oct-18 A Laboratory Testing - No. 1 & 2, 09-Oct-18 A
08-1040-34(1)(A)	Laboratory Testing - No. 3 & 4		1			20-Oct-18 A	20-Oct-18 A				100%	20-Oct-18 A Laboratory Testing - No. 3 & 4, 20-Oct-18 A
08-1040-35(1)(A)	Laboratory Testing - No. 5 & 6		1			24-Oct-18 A	24-Oct-18 A				100%	24-Oct-18 A Laboratory Testing - No. 5 & 6, 24-Oct-18 A
08-1040-36(1)(A)	Laboratory Testing - No. 7 & 8		1			25-Oct-18 A	25-Oct-18 A				100%	25-Oct-18 A Laboratory Testing - No. 7 & 8, 25-Oct-18 A
08-1040-37(1)(A)	Laboratory Testing - No. 9		1			30-Oct-18 A	30-Oct-18 A				100%	30-Oct-18 A Laboratory Testing - No. 9, 30-Oct-18 A
08-1040-38(1)(A)	Laboratory Testing - No. 10 & 11		0			08-Nov-18 A	08-Nov-18 A				100%	08-Nov-18 A Laboratory Testing - No. 10 & 11, 08-Nov-18 A
08-1040-39(1)(A)	Laboratory Testing - No. 12 & 13		4			10-Nov-18 A	14-Nov-18 A				100%	10-Nov-18 A Laboratory Testing - No. 12 & 13, 14-Nov-18 A
08-1040-40(1)(A)	Laboratory Testing - No. 14 & 15		0			21-Nov-18 A	21-Nov-18 A				100%	21-Nov-18 A Laboratory Testing - No. 14 & 15, 21-Nov-18 A
08-1040-43(1)(A)	Issue Test Report		4			22-Nov-18 A	26-Nov-18 A				100%	22-Nov-18 A Issue Test Report, 26-Nov-18 A
08-1040-44(3)(A)	Carry out CPT for Plant Trial retiral (10 nr. @ 2nr./day)		31			13-Feb-19 A	16-Mar-19 A				100%	13-Feb-19 A Carry out CPT for Plant Trial retiral (10 nr. @ 2nr./day), 16-Mar-19 A
08-1040-45(3)(A)	Carry out Plant Trial for DCM Barges		3			19-Feb-19 A	19-Mar-19 A				100%	19-Feb-19 A Carry out Plant Trial for DCM Barges, 19-Mar-19 A

	Primary Baseline		Critical Remaining Work		Actual Milestone
	WP3 BL Critical Works		Baseline Milestone		Critical Milestone

